



PE

ProjectEmail

FULL FUTURE PLAN

Accounts, Build, Launch and Growth

A practical delivery handbook from current MVP
to secure public launch and measured growth.

Prepared for the ProjectEmail founders and GitHub collaborators

Version 1.0 | 27 August 2026 | Decision and execution document

PROJECT BOUNDARY

ProjectEmail is an independent private project with its own brand, accounts, domains, infrastructure and legal identity. It has no relationship to TradeZero or any trading application.

SECTION 01

Executive launch decision

What exists, what is blocked, and the shortest responsible path to a working service.

Bottom line

The product foundation is deployed and the database connection is healthy. Address creation is blocked because Neon has no active receiving domain. The fastest private activation is one mail domain, Cloudflare inbound routing, a signed Worker-to-API webhook, and an ACTIVE domain row.

Current baseline

Layer	Current service	Status	Meaning
Frontend	GitHub Pages	Live	Track B experience is deployed.
API	FastAPI on Render	Live, free tier	Health and Neon readiness respond.
Database	Neon Postgres	Connected	Schema exists; no active mail domain.
Inbound mail	Cloudflare Email Service	Blocked	Worker, route and MX activation still required.
Safe HTML	Quarantine origin	Not deployed	Required before displaying untrusted HTML.
CI/CD	GitHub Actions	Green	Track A and Track B commits are on main.

Expected delivery window

Private activation

1 to 3 development days after access

One external email reaches the live inbox.

Secure public beta

3 to 5 engineering weeks

Production hosting, security, quarantine viewer, policies and monitoring.


Important planning correction

The attached investor document is a strategic input, not a verified forecast or an instruction set. Its traffic, revenue, infrastructure-cost and advertising-yield claims require real validation. This handbook deliberately replaces mass page generation, aggressive ad refresh and unsupported scale assumptions with measured product, policy and reliability gates.

SECTION 02

Target architecture

The production data path, trust boundaries and reasons each dependency exists.

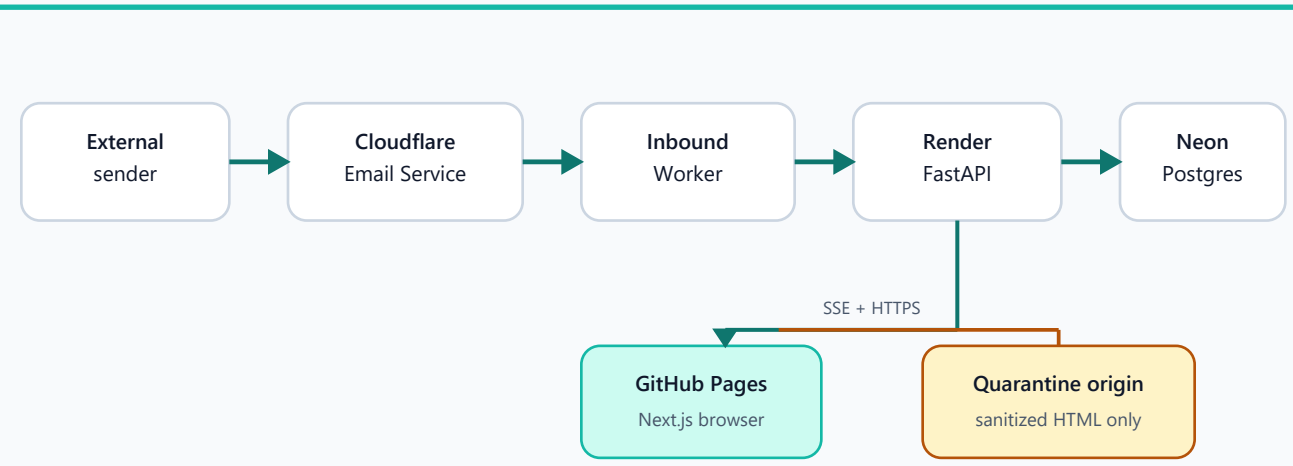

Mail path

- Cloudflare receives mail for an owned pool domain and sends the raw stream to a minimal inbound Worker.
- The Worker rejects oversized input, attaches a timestamp, delivery identifier and signature, then posts to FastAPI.
- FastAPI validates the request, parses and sanitizes MIME, stores short-lived data in Neon, and emits an SSE event.
- The browser holds the inbox possession token only in the current tab. Plain text is preferred; sanitized HTML renders only on a separate registrable quarantine origin.

Non-negotiable boundaries

Boundary	Required behavior
Inbound only	No send, reply, relay or forwarding. No SMTP client dependency.
Short retention	Expiry is a product promise and must be measured, alerted and verified.
No active content	Email scripts, forms, embedded remote content and unsafe URLs are blocked.
Separate origins	Brand site, receiving domain pool and quarantine renderer are distinct.
Least privilege	Provider roles and secrets are scoped; founders own every account.
No secret leakage	Connection strings, tokens and message bodies never enter Git, tickets or the PDF.

SECTION 03

Accounts to create

The founder-owned account inventory, creation order and access model.

Ownership rule

Create every production account with a ProjectEmail-controlled business mailbox, enable MFA, store recovery codes in a shared password manager, and invite collaborators by role. Never share a personal password.

Account	When	Owner	Purpose
Domain registrar	Now	Founder	Own brand, mail-pool and quarantine domains. Registrar can remain separate from Cloudflare DNS.
Cloudflare	Now	Founder	DNS, Email Service, Workers, Turnstile, WAF and optional Web Analytics.
GitHub organization or repo	Exists	Founder	Source, issues, Actions, Pages, branch protection and releases.
Neon	Exists	Founder	Production and staging Postgres. Enable organization MFA and production protection.
Render	Exists	Founder	Paid Ohio API service before public beta.
Password manager	Now	Founders	Shared vault for recovery codes and vendor secrets. Use 1Password, Bitwarden or equivalent.
Sentry or equivalent	Before beta	Founder	Scrubbed exception telemetry only. Never record addresses, tokens or message bodies.
Uptime monitor	Before beta	Founder	API health, ready checks and synthetic inbound-mail canary.
Google Search Console	After brand domain	Founder	Ownership verification, sitemap, indexing and search diagnostics.
Bing Webmaster Tools	After brand domain	Founder	Bing indexing and IndexNow monitoring.
Shared support mailbox	Before beta	Founder	Monitored privacy@, abuse@ and security@ addresses on a non-pool domain.
Ad platform and CMP	After traction	Founder	Only after policies, consent design and substantial public content are ready.

Official starting points

[Cloudflare dashboard](#) | [Neon console](#) | [Render dashboard](#) | [Google Search Console](#) | [Bing Webmaster Tools](#)

SECTION 04

Domains and DNS

Exactly which domains are needed, what each is allowed to do, and the minimum launch set.

Domain type	Quantity	Use	Rule
Brand domain	Required before public launch	Website, policies, docs and support identity	Never use it as the disposable mail pool.
Mail-pool domain	One for activation; three recommended for beta	Receives random temporary addresses	Cloudflare DNS and Email Service required.
Quarantine domain	Required before HTML viewer launch	Hosts sanitized email rendering	Separate registrable domain, not a subdomain.
Support mailbox domain	Can use brand domain	privacy@, abuse@, security@	Must not be one of the disposable pool domains.

Cloudflare setup sequence

1. Add the receiving domain to Cloudflare and change its authoritative nameservers at the registrar.
2. Open Compute > Email Service > Email Routing and enable routing for the domain.
3. Allow Cloudflare to add the required MX, SPF and DKIM records.
4. Deploy the ProjectEmail inbound Worker and store its webhook secrets in Worker Secrets.
5. Create a catch-all or controlled routing rule that sends matching addresses to the Worker.
6. Verify DNS, send a canary message, and keep the domain in WARMING until end-to-end delivery passes.
7. Activate the domain in Neon only after the canary succeeds.

Minimum activation purchase

One receiving domain is enough for a private smoke test. The brand domain and quarantine domain can follow, but both are required before a responsible public launch.

SECTION 05

Access, secrets and permissions

How the founders collaborate without exposing credentials or losing account ownership.

Provider	Invite permission needed	Do not share
Cloudflare	DNS edit, Email Service, Workers scripts and secrets	Account owner, billing or domain transfer unless explicitly needed
GitHub	Maintain/write; Actions and Pages administration when deployment work requires it	Organization ownership changes
Neon	Project administration for schema, branches and connection roles	Personal login or recovery codes
Render	Service and environment administration	Workspace ownership or billing changes without approval
Search tools	Verified property owner or delegated full user	Personal Google/Microsoft credentials
Monitoring	Project administration with scrubbed data	Unrestricted access to unrelated projects

Secret inventory

Names below are configuration keys only. Values belong in provider secret stores, never GitHub source, screenshots, chat messages or this document.

Location	Key	Purpose
Backend	DATABASE_URL	Neon pooled endpoint for normal application traffic
Backend	MIGRATION_DATABASE_URL	Neon direct endpoint for Alembic and administrative DDL
Backend	SECRET_KEY	Possession-token signing and application security
Backend + Worker	INBOUND_WEBHOOK_SECRET_CURRENT	Active signed-webhook secret
Backend + Worker	INBOUND_WEBHOOK_SECRET_NEXT	Overlap during zero-downtime secret rotation
Backend	APP_ORIGIN / SANDBOX_ORIGIN	Strict CORS and renderer origin allowlists
Frontend	NEXT_PUBLIC_API_URL	Public API base URL; not a secret
Frontend	NEXT_PUBLIC_SITE_URL	Canonical brand URL; not a secret
Optional	TURNSTILE_* / SENTRY_DSN	Bot control and scrubbed monitoring

SECTION 06

Software and infrastructure dependencies

What is already installed, what will be added, and when scaling dependencies become necessary.

Area	Dependency	Status	Why
Frontend	Node.js 22, pnpm 9.14.2, Next.js 15, React 19, TypeScript	Exists	Static app and inbox UI
Backend	Python 3.12, uv, FastAPI, SQLAlchemy, asyncpg, Alembic	Exists	API and Neon access
Mail	Cloudflare Wrangler, Workers types, test runtime	Add in Phase 1	Worker deploy and edge tests
Sanitization	nh3 plus browser sandbox controls	Partial	Safe email body processing
Testing	Pytest, Vitest, Playwright	Exists	Unit, integration and browser validation
Containers	Docker	Exists	Repeatable local and Render builds
Shared events	Redis or Render Key Value	Later only	Needed before API workers exceed one
Observability	Structured logs, uptime monitor, optional Sentry	Complete before beta	Operate safely without logging PII

Why Redis is not an activation dependency

The MVP intentionally uses one API worker because SSE fanout is currently in process. Redis becomes mandatory before horizontal scaling so an inbound webhook handled by one worker can notify browser streams connected to another. Until then, WEB_CONCURRENCY must remain 1.

Connection rules

- Use the Neon pooled hostname for web requests and worker traffic.
- Use the direct Neon endpoint for schema migrations, backup and restore tools.
- Keep the API and database in the same geographic region.
- Do not put any Neon connection string in NEXT_PUBLIC variables or browser code.

SECTION 07

Phase 0 and Phase 1: activate the service

The precise work sequence from founder decisions to the first real message in a browser tab.

Step	Owner	Action	Evidence
0.1	Founders	Choose brand, receiving and quarantine domains; approve hosting budget and launch countries.	Decision sheet complete
0.2	Founders	Create or secure provider accounts, enable MFA, invite role-based access.	Access verified
1.1	Codex	Add Worker package, typed configuration, size guard, normalized payload and deploy workflow.	Worker test suite green
1.2	Both	Configure Cloudflare DNS, Email Service, routing and Worker secrets.	MX and route active
1.3	Codex	Add webhook timestamp, signature, delivery ID, idempotency and rotation support.	Replay tests green
1.4	Codex	Add safe domain administration command and seed the receiving domain as WARMING.	Domain visible in Neon
1.5	Both	Send Gmail/Outlook canaries and inspect Worker, API, database, SSE and UI behavior.	Real mail appears
1.6	Codex	Activate domain and verify expiry/deletion paths.	Create-inbox no longer returns 503

Activation definition

A randomly generated address is created, an email sent from outside the system is accepted, the message arrives through SSE, the body can be read safely, and both inbox and message disappear on schedule.

Phase 1 test matrix

Test group	Cases
Sender	Gmail, Outlook and one OTP/newsletter provider
Content	Plain text, multipart HTML, Unicode, malformed MIME, empty body
Limits	Just below and above 10 MiB; excessive headers; duplicate delivery
Lifecycle	10, 30 and 60 minute TTL; manual delete; reconnect after network loss
Failure	Bad secret, expired timestamp, replayed ID, inactive domain, unknown recipient

SECTION 08

Phase 2: security and abuse hardening

Controls that must pass before unknown users can create inboxes.

Area	Control	Proof
Webhook	10 MiB limit, signed timestamp, constant-time verification, idempotency, dual-secret rotation	Automated API and Worker tests
Inbox access	High-entropy address, possession token, no public listing, enumeration detection	Negative and brute-force tests
Rate limiting	Per-IP, per-token and per-destination limits with Turnstile escalation	Burst and sustained-load tests
MIME	Bounded parsing, filename normalization, attachment metadata limits	Malicious fixture corpus
HTML	Server sanitization, no scripts/forms, remote images off, no base URL surprises	XSS and URL test suite
Links	Warning interstitial, normalized URL, explicit user action	Browser tests
Logging	No body, possession token or complete address in logs	Log-content audit
Abuse	Inbound only, domain draining, kill switch, monitored abuse channel	Runbook exercise

Quarantine-origin policy

The renderer must use a separate registrable domain and a CSP equivalent to: default-src 'none'; script-src 'none'; style-src 'unsafe-inline'; img-src 'self' data:; form-action 'none'; base-uri 'none'. The iframe must not receive allow-scripts, allow-same-origin, forms or modal permission.

Public-launch blocker

Do not display sender-controlled HTML on the brand origin. Sanitization alone is insufficient; origin isolation and browser sandbox restrictions are both mandatory.

SECTION 09

Phase 3: production reliability

Remove prototype limits, align regions and make service health measurable.

Recommended production move

The current API is configured in Render Oregon while Neon is in AWS us-east-2 (Ohio). Create a replacement paid Render service in Ohio, migrate environment configuration, test it, then change the frontend API URL. Render does not change an existing service's region in place.[6]

Area	Production configuration	Exit condition
Render	Paid Ohio web service, one worker, health and readiness endpoints, controlled migrations	No free-tier sleep during OTP delivery
Neon	Paid plan, protected production branch, staging branch, MFA, appropriate autoscaling	Restore drill succeeds
Deploy	CI checks, reviewed migration, smoke test, rollback procedure	Release checklist attached to each deploy
Monitoring	Health, readiness, error rate, latency, connection usage, deletion lag	Alert owner and escalation path assigned
Mail canary	Scheduled real message to a test inbox	Delivery time and missing-mail alerts
Backups	History retention plus periodic restore verification	Recovery-time objective measured
Secrets	Rotation calendar and incident rotation procedure	No expired or owner-personal credentials

Initial service objectives

Metric	Initial target
Inbox creation	>= 99.5% successful requests excluding deliberate rate limits
API latency	p95 below 500 ms for create/list under expected beta load
Inbox page	p95 usable load below 2 seconds on a representative mobile network
Mail delivery	Measure sender-to-visible latency; alert on missing canary
Deletion	Expired content removed within the documented grace window

SECTION 10

Phase 4: product completion

Finish Track B without weakening Track A security controls.

Product area	Delivery
API contracts	Generate frontend TypeScript types from FastAPI OpenAPI; fail CI on contract drift.
Message viewer	Plain-text default, sanitized HTML tab, blocked-image status, safe link interstitial.
Inbox controls	Copy address, timer, delete, create-again, reconnect status and expired-session recovery.
Responsive UI	Playwright coverage at 390, 768 and 1440 px; keyboard and screen-reader checks.
Performance	Reserve layout space, minimize client JavaScript, monitor Core Web Vitals.
Policy pages	Privacy, terms, acceptable use, cookies, abuse, security and service status.
API and extension	Defer public developer API and browser extension until the web service is reliable and abuse controls are proven.

User-experience principles

- One primary action on the home page: create a private inbox.
- No registration, no deceptive countdown and no confusing domain selector at first launch.
- Always show the exact retention timer and explain what deletion means.
- Make inbound-only behavior visible so users do not expect reply or forwarding.
- Keep advertising and analytics code out of inbox and message security boundaries.

SECTION 11

Phase 5: SEO and AI discovery

Build authority through useful public information, not mass-generated pages or an imaginary approval switch.

Reality check

Google has no special AI schema or AI approval process. Search and AI visibility depend on crawl access, useful indexed content, clear internal linking, strong page experience and claims that can be supported.[10] OpenAI search visibility requires allowing OAI-SearchBot; GPTBot training permission is a separate choice.[15]

Workstream	Plan
Foundation	Permanent custom domain, HTTPS, canonical URLs, sitemap, robots.txt, clean status codes
Discovery	Google Search Console, Bing Webmaster Tools, IndexNow after content changes
AI crawlers	Allow OAI-SearchBot; decide GPTBot separately; do not block required IP ranges at WAF
Structured data	Organization, WebSite, SoftwareApplication and visible FAQ data where accurate
Content	Start with 4 original cornerstone guides, then expand to 10 to 20 only after quality review
Evidence	Named authors/reviewers, update dates, source links, tested screenshots and measured claims
Localization	Translate only proven pages with human review, correct canonicals and hreflang
Avoid	Thousands of templated pages, copied comparisons, unsupported superlatives and thin city/language variants

First content cluster

Temporary email basics

CORNERSTONE 1

What it is, legitimate use cases, limitations and retention.

OTP and verification

CORNERSTONE 2

How to receive codes safely and why delivery can fail.

QA and software testing

CORNERSTONE 3

Ethical temporary inbox workflows for test automation.

Email privacy

CORNERSTONE 4

Remote-image tracking, aliases versus temporary inboxes, and safe links.

SECTION 12

Legal, privacy and abuse readiness

Information founders must decide and counsel must review before a public launch.

Topic	Decision/evidence required	Owner
Operator identity	Legal entity or individual name, jurisdiction, address and contact details	Founder
Audience	Launch countries, minimum age and excluded uses	Founder + counsel
Data inventory	Address, sender, headers, body, attachment metadata, IP/security telemetry	Codex + founder
Retention	Published TTL, backup/history behavior, deletion grace and incident exceptions	Founder + counsel
Processors	Cloudflare, Render, Neon, GitHub and selected monitoring/analytics vendors	Founder
Rights process	Privacy requests, complaints, abuse reports and lawful-request handling	Counsel
Policies	Privacy, terms, acceptable use, cookies, abuse and security disclosure	Counsel approves
Consent	Analytics/ad consent by applicable geography	Counsel + ad partner

Not legal advice

Codex can draft page structure, data-flow descriptions and operational checklists. The founders must provide truthful business facts, and qualified counsel must approve jurisdiction-specific legal language before publication.

Abuse-response minimum

- A monitored abuse@ mailbox with documented response ownership.
- Ability to drain or retire a mail domain without breaking existing cleanup.
- Rate-limit and create-inbox kill switches.
- A preserved audit trail of security events without retaining message content unnecessarily.
- Published statement that the service cannot send, reply or forward email.

SECTION 13

Monetization plan

Delay ad complexity until policy, content and product evidence make monetization sustainable.

Stage	Trigger	Action	Constraint
Stage 0	Activation to closed beta	No ads	Protect usability, measure delivery, avoid approval risk
Stage 1	Indexed content and repeat users	Relevant affiliate or direct sponsor tests on guide pages only	Simple attribution and clear disclosure
Stage 2	Substantial public content	Apply to a suitable ad network with a compliant consent setup	No placement on inbox/message/quarantine screens
Stage 3	Material traffic and ops capacity	Evaluate Google Ad Manager or header bidding	Only with specialist policy review and measured page performance

Permanent ad exclusions

- Inbox workspace, message body, quarantine renderer, deletion confirmation and link interstitial.
- Any screen with little publisher-created content or primarily behavioral navigation.
- Layouts that resemble system controls, cause accidental clicks or obstruct the inbox timer.

Investor-model treatment

Do not use the attached plan's MAU, eCPM, margin, impression, domain-cost or ARR figures as commitments. Replace them with a live model after 30 to 90 days of measured sessions, geography, viewability, fill rate, infrastructure usage and support load. Google publisher policy also makes low-value and behavior-only screens unsuitable for ad placement.[14]

SECTION 14

Testing and launch gates

Evidence required at private activation, closed beta and public release.

Gate	Required evidence	Release condition
Functional	Create address, receive real mail, SSE reconnect, copy, delete, expiry	All supported browsers pass
Security	Webhook replay/rotation, XSS, oversized MIME, token enumeration, SSRF	No critical/high unresolved
Privacy	Log audit, retention verification, remote images blocked	Policy matches observed behavior
Reliability	Load, cold start, database retry, worker failure, restore drill	SLO evidence stored
UX	390/768/1440 px, keyboard, screen reader, error states	No blocking accessibility defects
Operations	Canary, alerts, on-call owner, domain drain and rollback	Runbook rehearsal complete
Legal	Published policies and monitored contacts	Counsel/founder sign-off
SEO	Custom domain, HTTPS, canonical, sitemap, robots, verification	Search tools see clean property

Closed-beta protocol

Item	Plan
Participants	10 observed testers across mobile and desktop
Senders	Gmail, Outlook and representative OTP/newsletter services
Duration	7 to 14 calendar days
Measures	Success rate, time-to-address, delivery latency, inbox-open time, confusion and failures
Exit	All blocker defects fixed; alerts and abuse response exercised

SECTION 15

Responsibility and delivery model

Exactly what Codex will provide, what founders provide, and what remains third-party controlled.

Workstream	Founder provides	Codex provides	External control
Domains and subscriptions	Choose and pay; accept vendor terms	Advise, configure after authorization	Registrar/providers
Architecture and code	Approve product decisions	Design, implement, test, document, pull and push	GitHub/CI
Cloudflare mail	Own account and domain	Build Worker, configure routes/secrets, test	Cloudflare availability
Database	Own Neon account and billing	Schema, migration, branches, domain lifecycle, restore test	Neon platform
Deployment	Approve production plan	Render service, env, health, cutover and rollback	Render platform
Security	Set risk tolerance and response owner	Controls, tests, threat model and runbooks	Independent review optional
Legal	Provide facts and obtain counsel approval	Draft structure and technical data map	Counsel/regulators
SEO/content	Approve voice and claims	Technical SEO, content briefs, drafts and measurement	Search engines
Ads	Own accounts and accept policies	Safe integration after approval	Ad network approval

Code delivery protocol

- Pull the latest GitHub main branch before each new engineering request.
- Work in focused commits with tests and no unrelated file changes.
- Run proportional unit, integration, browser and deployment checks.
- Push completed work to GitHub and report commit, verification and remaining blockers.
- Use the established ProjectEmail navy, teal and slate design language across app and project documents.

SECTION 16

Critical path and schedule

A dependency-aware sequence for one to two active collaborators.

Window	Primary work	Milestone
Week 0	Founder decisions, domains, accounts, MFA, invitations	Receiving domain and access
Week 1	Cloudflare Worker, DNS, webhook signing, Neon domain activation	First real email
Week 2	Rate limits, replay/idempotency, integration tests, abuse controls	Security baseline
Week 3	Paid Ohio Render, Neon protection/staging, monitoring, restore	Production reliability
Week 4	Quarantine viewer, safe links/images, browser and accessibility tests	Track A/B completion
Week 5	Brand domain, policies, technical SEO, first four guides	Closed-beta candidate
Weeks 6 to 7	Ten-user beta, sender matrix, fixes, launch review	Public-release decision
Post-launch	Measured content, API/extension evaluation, monetization only after gates	Evidence-led growth

Model-tier allocation

Tier	Assigned work
Flagship reasoning	Mail architecture, quarantine isolation, threat model, production cutover and final launch review
Balanced engineering	API/UI implementation, integrations, unit tests, routine debugging and refactors
Lightweight execution	Documentation, content formatting, checklists and mechanical updates

Schedule assumption

Estimates begin after required domain ownership, provider access and founder decisions are available. DNS propagation, legal review and third-party approvals can extend calendar time.

SECTION 17

Budget and procurement worksheet

Approve categories and ceilings before any purchase; obtain current vendor quotes at decision time.

Category	Scope	Cadence	Approval note
Domains	Brand + quarantine + 1 to 3 mail domains	Annual	Founder enters ceiling
Render	Paid Ohio API service	Monthly	Required before public beta
Neon	Paid/protected production database	Monthly	Required before public beta
Cloudflare	DNS/Email Service; Workers plan as usage requires	Monthly/usage	Start lean; review quotas
Monitoring	Uptime and scrubbed error monitoring	Monthly	Required operational function
Legal	Privacy/terms/abuse and jurisdiction review	Project fee	Required external review
Content	Editing, expert review, illustrations if needed	Project/monthly	Scale only with measured quality
Ads/CMP	Consent and ad-ops tools	Later	Do not procure before traction

Procurement rules

- Founders own billing and approve every paid plan or domain purchase.
- Use current vendor pricing at purchase time; do not rely on estimates in the investor PDF.
- Set provider spend alerts and a monthly infrastructure ceiling.
- Avoid annual commitments until the inbound pipeline and beta demand are proven.
- Keep a vendor register containing owner, plan, renewal date, data processed and cancellation steps.

SECTION 18

Risk register

The highest-impact failure modes and the mitigation owner.

Risk	Likelihood / impact	Mitigation	Owner
No active mail domain	Certain / High	Buy and route one domain; domain admin path	Both
Webhook injection/replay	High / Critical	Signed fresh requests, idempotency, rotation	Codex
Email HTML XSS	High / Critical	Sanitizer + separate quarantine origin + CSP	Codex
Free-host cold start	High / High	Paid Ohio Render before beta	Founder
Cross-region latency	Current / Medium	Move Render API to Ohio	Both
Domain reputation loss	Medium / High	Pool lifecycle, monitoring, draining, no outbound	Both
Bot/abuse spike	High / High	Rate limits, Turnstile, kill switch, WAF	Codex
Retention promise mismatch	Medium / Critical	Deletion SLO, alerts and restore-aware disclosure	Both
Search spam classification	Medium / High	Original content; no mass templated pages	Both
Ad-policy rejection	Medium / Medium	Delay ads; content-only placement; consent review	Founder
Legal gap	Medium / Critical	Truthful data map and counsel sign-off	Founder
Account lockout	Medium / High	Business-owned accounts, MFA, shared recovery vault	Founder

Launch decision

A public launch is GO only when all Critical and High launch blockers are closed, the founder has approved the legal and billing decisions, and the complete outside-sender test passes on the production domain and production API.

SECTION 19

Founder response sheet

The information required to begin Phase 1 without sending passwords or secret values.

Permanent brand domain:	
Receiving mail domain(s):	
Quarantine domain:	
Cloudflare invitation sent:	☐ Yes ☐ No
Render invitation sent:	☐ Yes ☐ No
Neon organization MFA enabled:	☐ Yes ☐ No
Password manager/shared vault ready:	☐ Yes ☐ No
Monthly infrastructure ceiling:	
Legal operator/entity name:	
Country and province/state:	
Initial launch countries:	
Privacy contact:	
Abuse contact:	
Security contact:	
Default inbox lifetime:	☐ 10 ☐ 30 ☐ 60 minutes
Paid Render authorized:	☐ Yes ☐ No
Paid Neon authorized:	☐ Yes ☐ No
Target private activation date:	

Send decisions,
not credentials

Return the completed answers in chat or an issue. Provider invitations and dashboard secret stores handle access. Do not include passwords, connection strings, API tokens or recovery codes.

SECTION 20

Definition of finished

The project is complete only when the product, security, operations and growth foundations all work together.

Done	Area	Acceptance condition
☐	Functional	Users create a random address, receive real external mail, read it safely and delete it.
☐	Lifecycle	10/30/60 minute expiration and deletion behavior matches the published promise.
☐	Security	Signed replay-safe webhook, rate limits, sandbox renderer and attack tests pass.
☐	Privacy	No secret or message-body leakage; data inventory and retention are documented.
☐	Reliability	Paid production service, aligned region, alerts, mail canary and restore drill.
☐	Operations	Domain warming/draining/retirement, incident, abuse and rollback runbooks tested.
☐	Legal	Truthful policies and contacts published with founder/counsel approval.
☐	Quality	Unit, integration, browser, accessibility, performance and beta gates pass.
☐	SEO	Custom HTTPS domain, canonical, sitemap, robots, search verification and four original guides.
☐	AI discovery	OAI-SearchBot allowed; useful public sources are crawlable and supported by evidence.
☐	Monetization	No ads on inbox/message surfaces; any later integration has consent and policy review.
☐	Ownership	Founders own accounts, billing, MFA and recovery; collaborator access is role-based.

Next milestone

After the founder response sheet is complete, the first delivery is a working Cloudflare-to-Render-to-Neon mail path demonstrated with one real outside email.

SECTION 21

Sources and evidence

Current provider documentation and ProjectEmail repository decisions used for this handbook.

Ref	Source	Document
1	ProjectEmail repository	docs/DEPLOYMENT.md, TRACK_A.md, TRACK_B.md, ROADMAP.md, SECURITY.md, DATABASE.md and ADRs 0001-0005
2	Cloudflare	Route emails
3	Cloudflare	Email handler API
4	Cloudflare	Email Service limits
5	Render	Free instance limitations
6	Render	Regions and region changes
7	Neon	Production checklist
8	Neon	Connection pooling
9	GitHub	Pages custom domains
10	Google Search	AI features and your website
11	Google Search	Scaled content abuse
12	Google Search	Build and submit a sitemap
13	IndexNow	Protocol documentation
14	Google Publisher	Publisher policies
15	OpenAI Docs	OpenAI crawlers
16	Investor-plan input	Disposable Email Platform - Investor Business Plan & Ad Optimization Strategy.pdf. Used as strategic context only; financial and traffic claims were not treated as verified.

Research reviewed 27 August 2026. Provider capabilities, limits, pricing and policies can change; re-check live documentation before purchasing plans or launching policy-sensitive features.

ProjectEmail is an independent private project. No TradeZero names, assets, systems, accounts, data or affiliation are used.
